




ART	Runway Widening					
	Overall		Civil		Electrical	
	Planned %	Actual %	Planned %	Actual %	Planned %	Actual %
04/04/2005			0.0%			
05/04/2005	0.5%	1.1%	0.7%	1.7%		
06/04/2005	1.7%	3.1%	2.4%	2.4%		
07/04/2005	3.7%	5.1%	5.2%	5.2%		
08/04/2005	6.9%	9.1%	9.8%	9.8%		
09/04/2005	10.9%	13.0%	15.6%	15.6%		
10/04/2005	17.4%	18.5%	24.9%	24.9%		
11/04/2005	23.6%	23.9%	33.7%	33.7%	0.0%	
12/04/2005	31.9%	27.9%	43.4%	38.6%	5.2%	2.9%
13/04/2005	38.4%	34.5%	50.4%	47.5%	10.4%	4.4%
14/04/2005	45.4%	37.0%	58.2%	50.7%	15.6%	5.1%
15/04/2005	51.4%	44.6%	62.7%	54.7%	24.4%	21.2%
16/04/2005	57.5%	48.3%	68.3%	59.9%	32.2%	21.2%
17/04/2005	62.4%	52.6%	72.6%	63.9%	38.5%	26.0%
18/04/2005	67.9%	60.2%	78.3%	71.7%	43.7%	33.4%
19/04/2005	71.8%	61.1%	81.7%	72.7%	48.9%	33.9%
20/04/2005	79.9%	67.6%	89.2%	76.4%	57.8%	47.0%
21/04/2005	85.4%	76.3%	94.0%	84.6%	65.6%	57.0%
22/04/2005	88.1%	86.6%	95.0%	93.1%	71.9%	71.5%
23/04/2005	90.2%	88.0%	95.8%	93.7%	77.0%	74.6%
24/04/2005	92.3%	88.0%	96.8%	93.7%	82.2%	74.6%
26/04/2005	95.3%	93.1%	98.2%	96.2%	88.5%	85.9%
27/04/2005	97.3%	97.6%	98.8%	97.2%	93.7%	98.4%
28/04/2005	99.2%		99.3%		98.9%	
29/04/2005	100.0%		100.0%		100.0%	

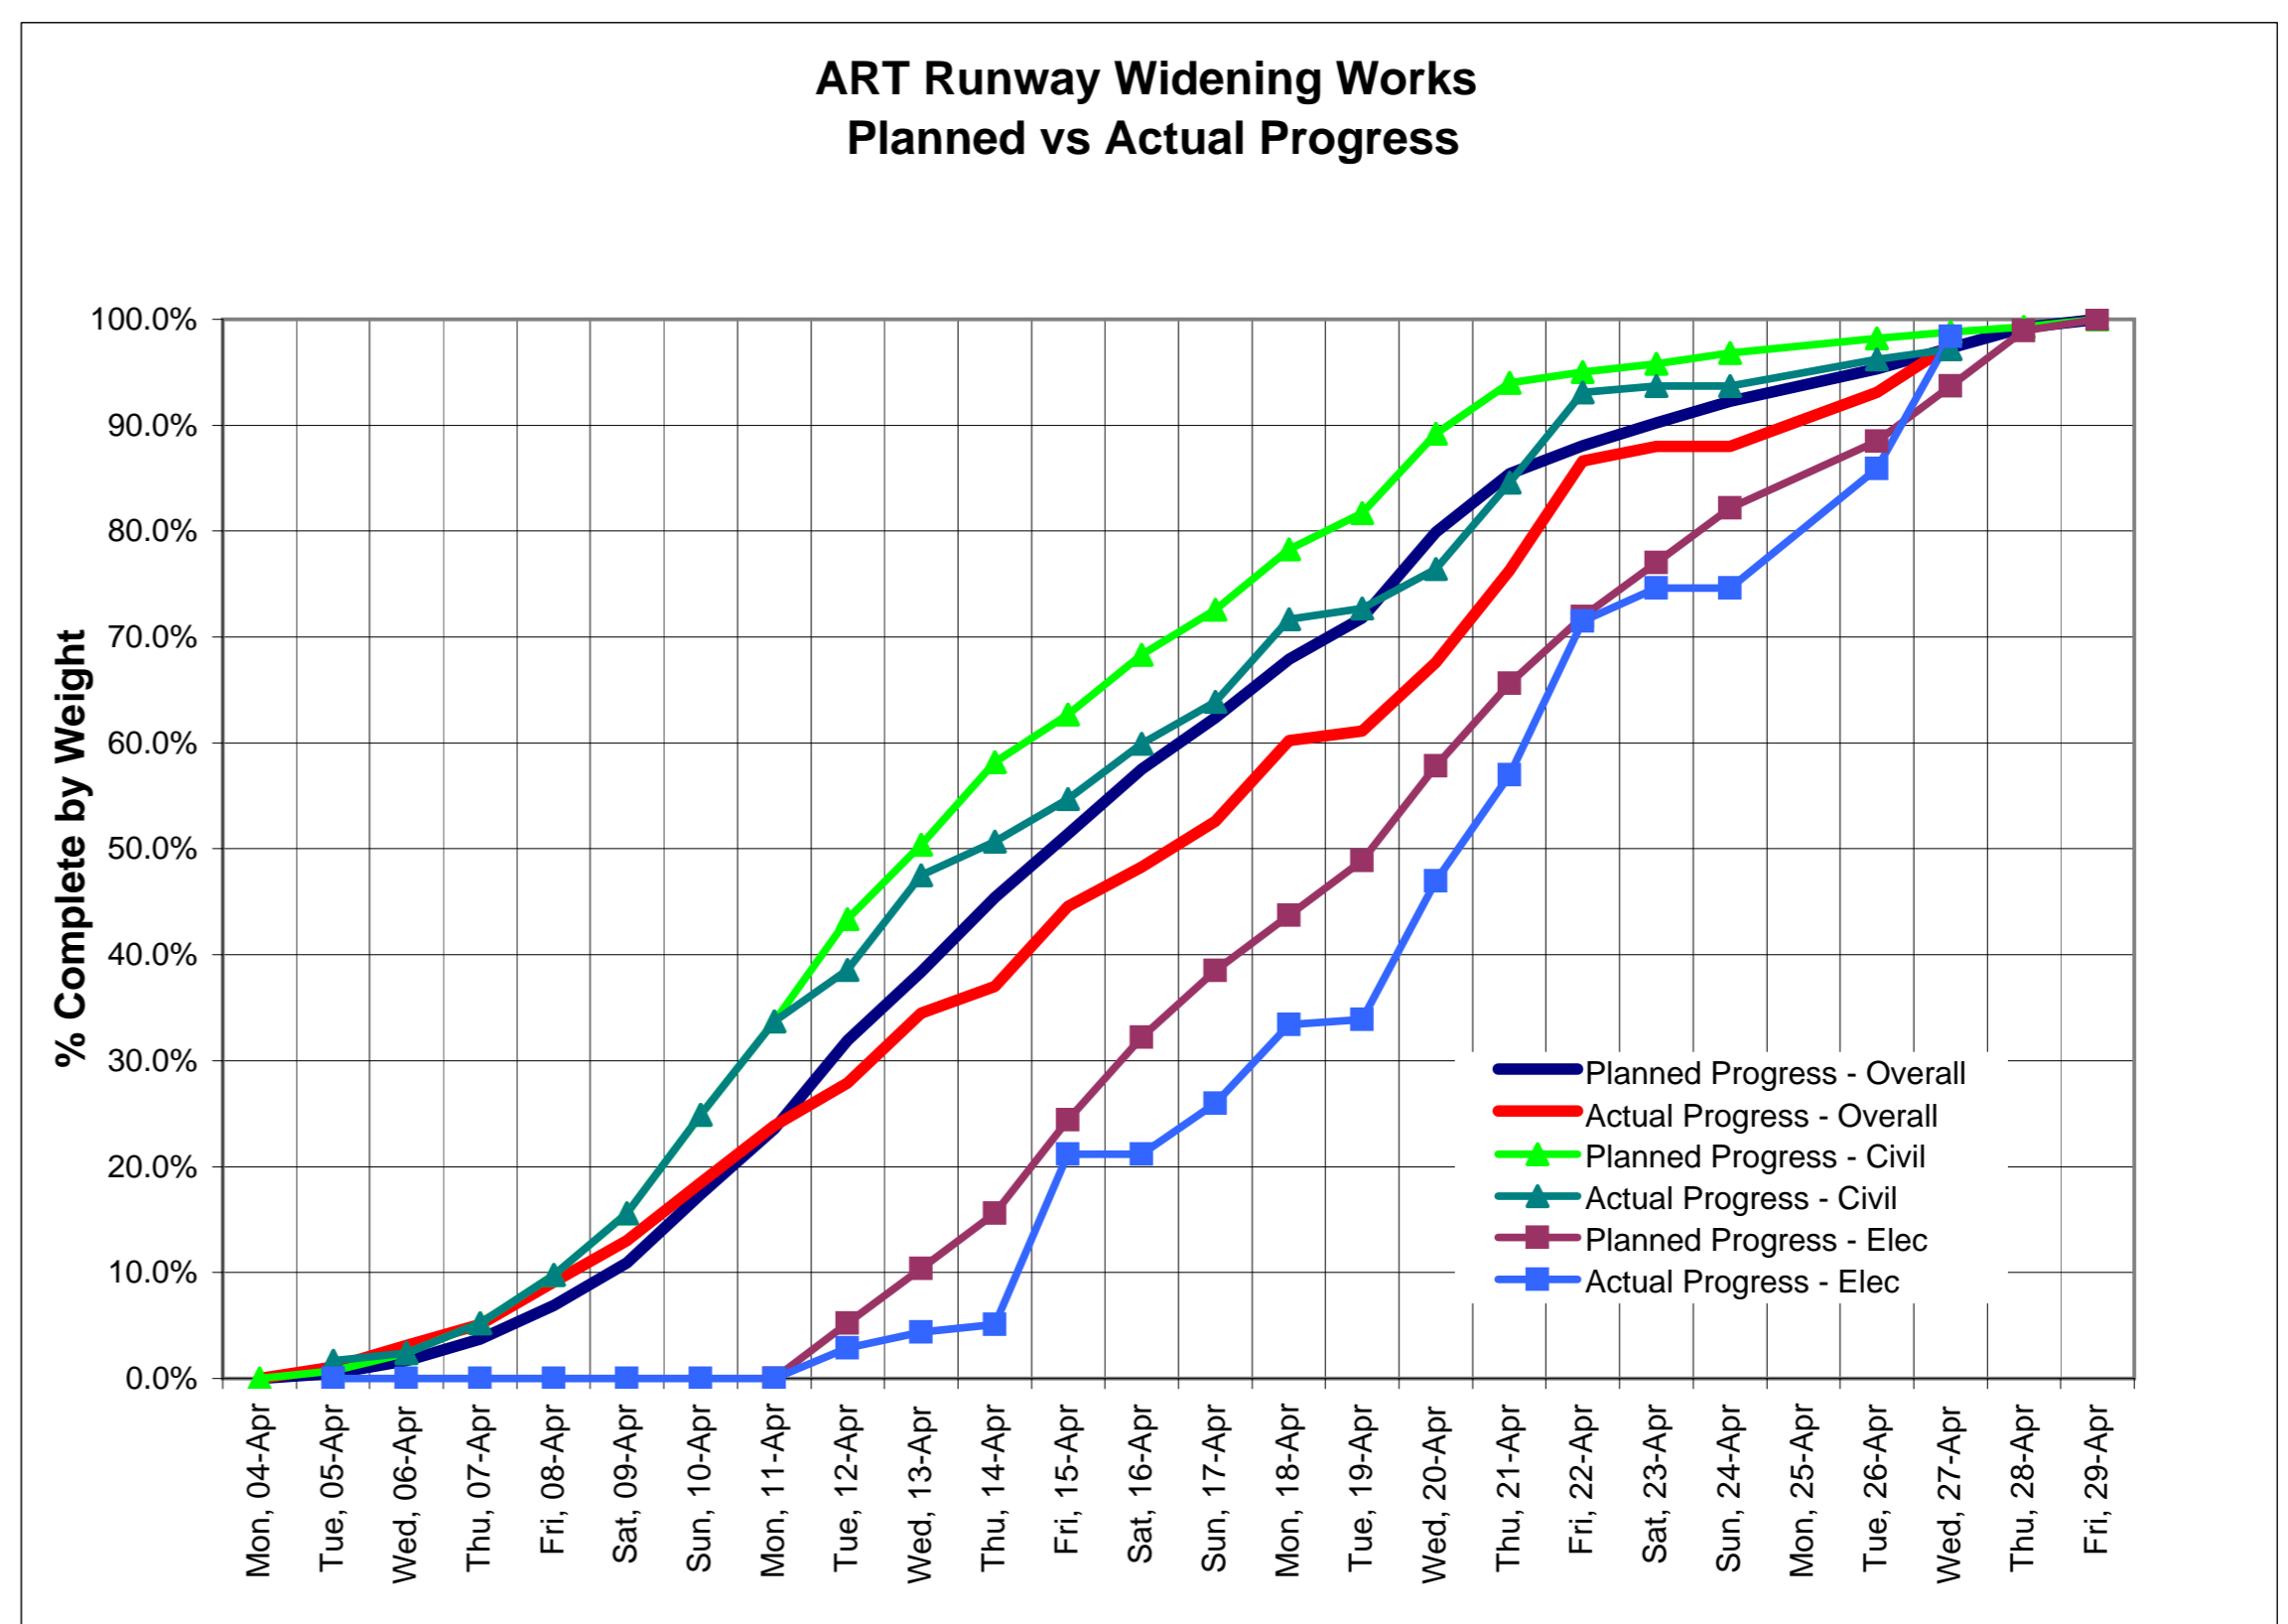

ART	Excavation	Kerb	Concrete	Concrete
	Actual %	Actual %	Actual %	Planned %
04/04/2005				0.0%
05/04/2005	8.1%			0.0%
06/04/2005	32.2%	6.0%	0.0%	0.0%
07/04/2005	45.6%	16.5%	0.0%	0.0%
08/04/2005	54.5%	45.6%	0.0%	0.0%
09/04/2005	68.9%	49.8%	0.0%	0.0%
10/04/2005	76.1%	54.9%	8.0%	6.2%
11/04/2005	76.5%	68.5%	17.3%	12.5%
12/04/2005	97.8%	80.3%	27.1%	24.4%
13/04/2005	100.0%	95.0%	37.5%	30.2%
14/04/2005		100.0%	39.1%	40.2%
15/04/2005			47.7%	44.4%
16/04/2005			51.2%	53.6%
17/04/2005			60.6%	58.5%
18/04/2005			68.8%	68.7%
19/04/2005			72.6%	74.0%
20/04/2005			76.5%	86.1%
21/04/2005			87.5%	93.1%
22/04/2005			99.0%	100.0%
23/04/2005			100.0%	
24/04/2005				
26/04/2005				
27/04/2005				
28/04/2005				
29/04/2005				

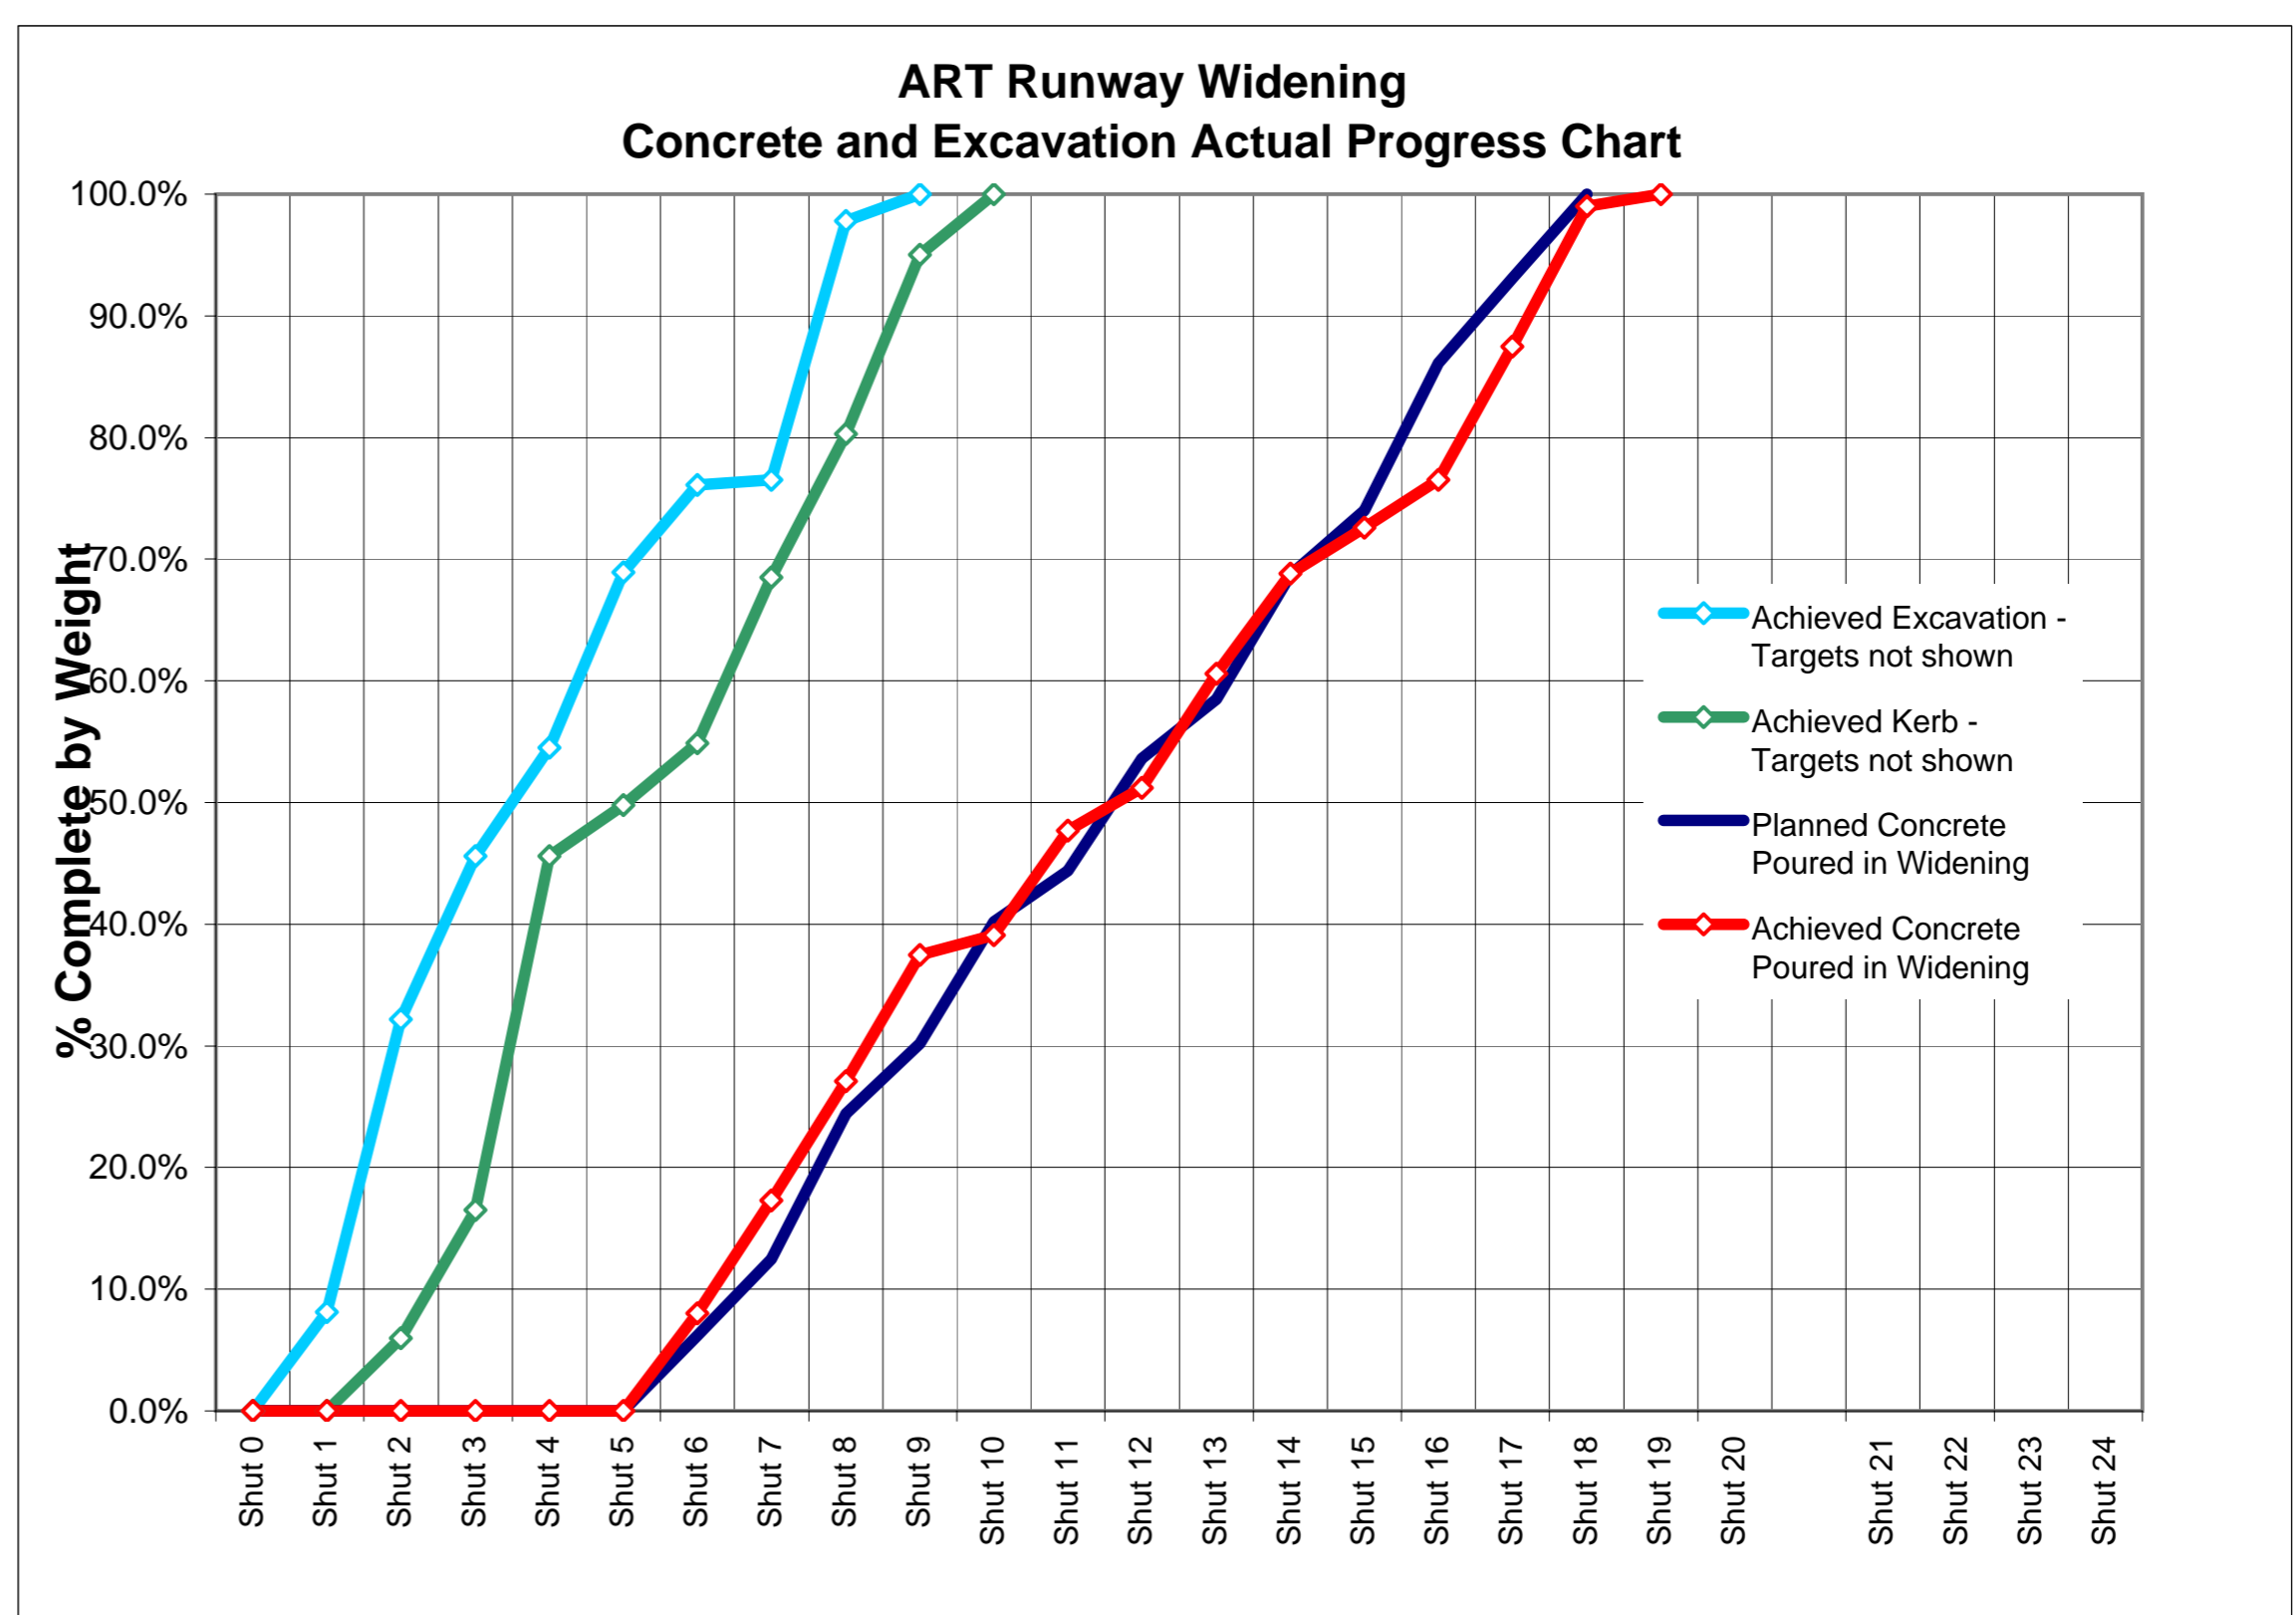

ART 0	Slab Replacement	
	Planned %	Actual %
04/04/2005	0.0%	
05/04/2005	1.3%	8.1%
06/04/2005	3.9%	22.7%
07/04/2005	8.3%	27.6%
08/04/2005	13.9%	41.4%
09/04/2005	21.3%	45.0%
10/04/2005	30.6%	50.0%
11/04/2005	41.9%	51.8%
12/04/2005	52.4%	51.8%
13/04/2005	60.0%	51.3%
14/04/2005	67.2%	60.2%
15/04/2005	74.8%	61.5%
16/04/2005	80.3%	67.8%
17/04/2005	84.3%	68.3%
18/04/2005	87.7%	69.0%
19/04/2005	91.7%	79.3%
20/04/2005	94.3%	84.2%
21/04/2005	96.5%	93.0%
22/04/2005	97.7%	93.3%
23/04/2005	98.8%	94.1%
24/04/2005	99.4%	94.1%
26/04/2005	99.9%	98.1%
27/04/2005	100.0%	98.9%
28/04/2005	0.0%	
29/04/2005	0.0%	

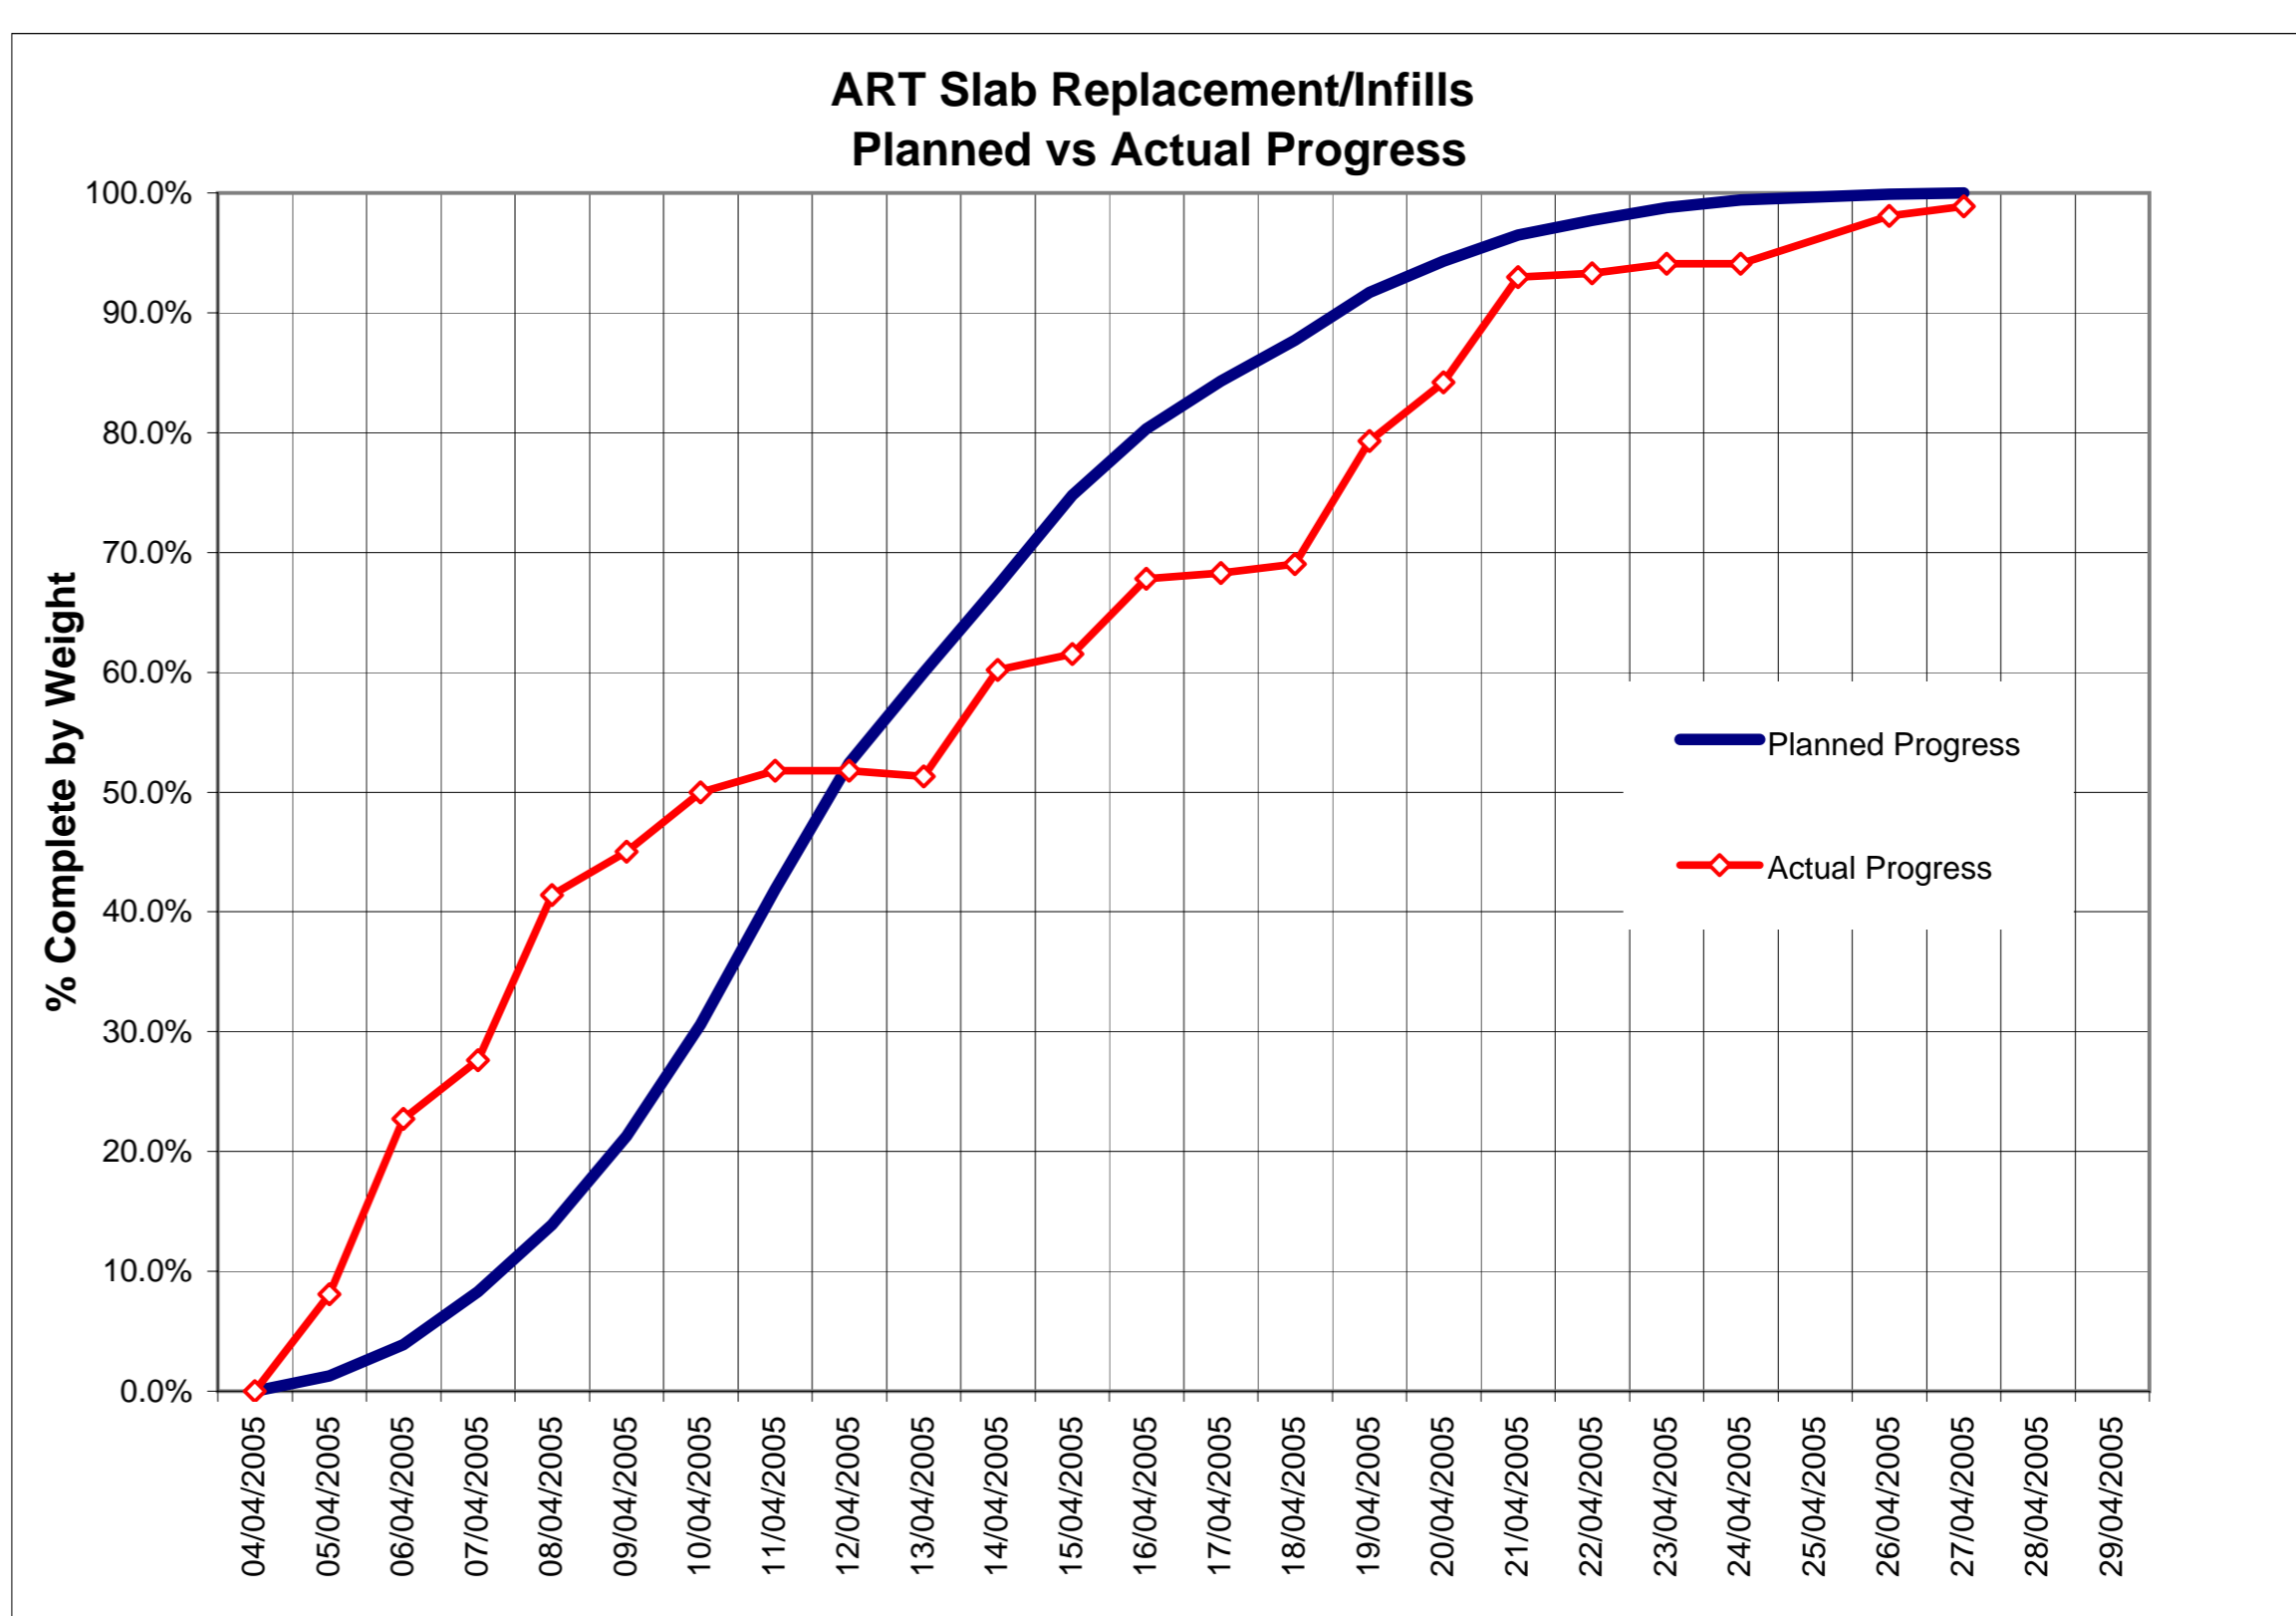

**For progress up to 4am:
Thursday, 28 April 2005**
